

17722

F. H. THORN

WELL DRILLING

BOX 209

MOORE, ALASKA

ARCO Alaska

Standard Oil Co. Water well Log 4-A. SRU 14-15.
Start 6:33 A.M. July 6, 1933.

0-2 Surface fill, gravel.
2-4 Clay.
4-10 Sand & Clay.
10-20 Sand, clay & gravel.
20-30 Sand & silt, some clay.
30-40 Coarse gravel.
40-50 Large gravel.
50-60 Clay, gravel & sand.
60-70 Gravel, small to large.
70-80 Sand & clay, some gravel.
80-90 Blue clay, some sand.
90-100 Gravel.
100-110 Gravel, sand & some clay.
110-120 Gravel-water.
120-130 Sand, gravel & clay.
130-140 Sand, fine, some water.
140-150 Fine gravel, sand, some large gravel, in streaks.
150-160 Large gravel.
160-170 Clay & sand.
170-180 Fine gravel, sand & large gravel, water.
180-190 Set up tools, run liner & start pull back casing. 1.00 P.M.
to 2 P.M. 4 hrs.
7-11-33 Pull casing & bail 7.00 A.M. to 8:30 P.M. 11 hrs.
7-12-33 Surge & bail 7.00 A.M. to 6:30 P.M. 11 hrs.
7-13-33 Install pump, pump well 7.00 A.M. to 5.00 P.M. 8 hrs.
Pull pump.

Remarks: Liner set on two ft. plug in casing, Plug left in casing
to keep sand & gravel from up-surgings.
28ft. perforated lines installed with bottom at 182ft. Perforations
exposed from 162ft in large gravel to 182.

Well Pumped lhr at 2400 g.P.M.
2 2hrs. " 3600 " "
2hrs. " 4000 " "

Water has iron content.

ABANDONED as per
ARCO letter dated
8/28/34 on file
with MAM

12/27/91 MB

SB 89-15CC

F. W. THORN

WILLIAM J. HARRIS

Standard Oil Well # 4-A casing run. SRU 14515.

RECEIVED JUN 20 1950

20-1
6-0
8-0
9-1
3-0
8-0
4-1
5-0
3-1
8-1
7-2
9-1
9-1
8-1
8-1
8-1
8-1
8-1
8-1

[illegible]


161-7
5-0
~~166-7~~
4-7 Pulled back + 6
~~171-2~~
5-0 Pulled back.
~~176-2~~
4-10 Pulled back
~~181-0~~
5-0 Pulled back.
~~186-0~~
12-11 Total pull back.
~~186-1~~



SB 8-9-15cc

17722

Swanson River Field Wells

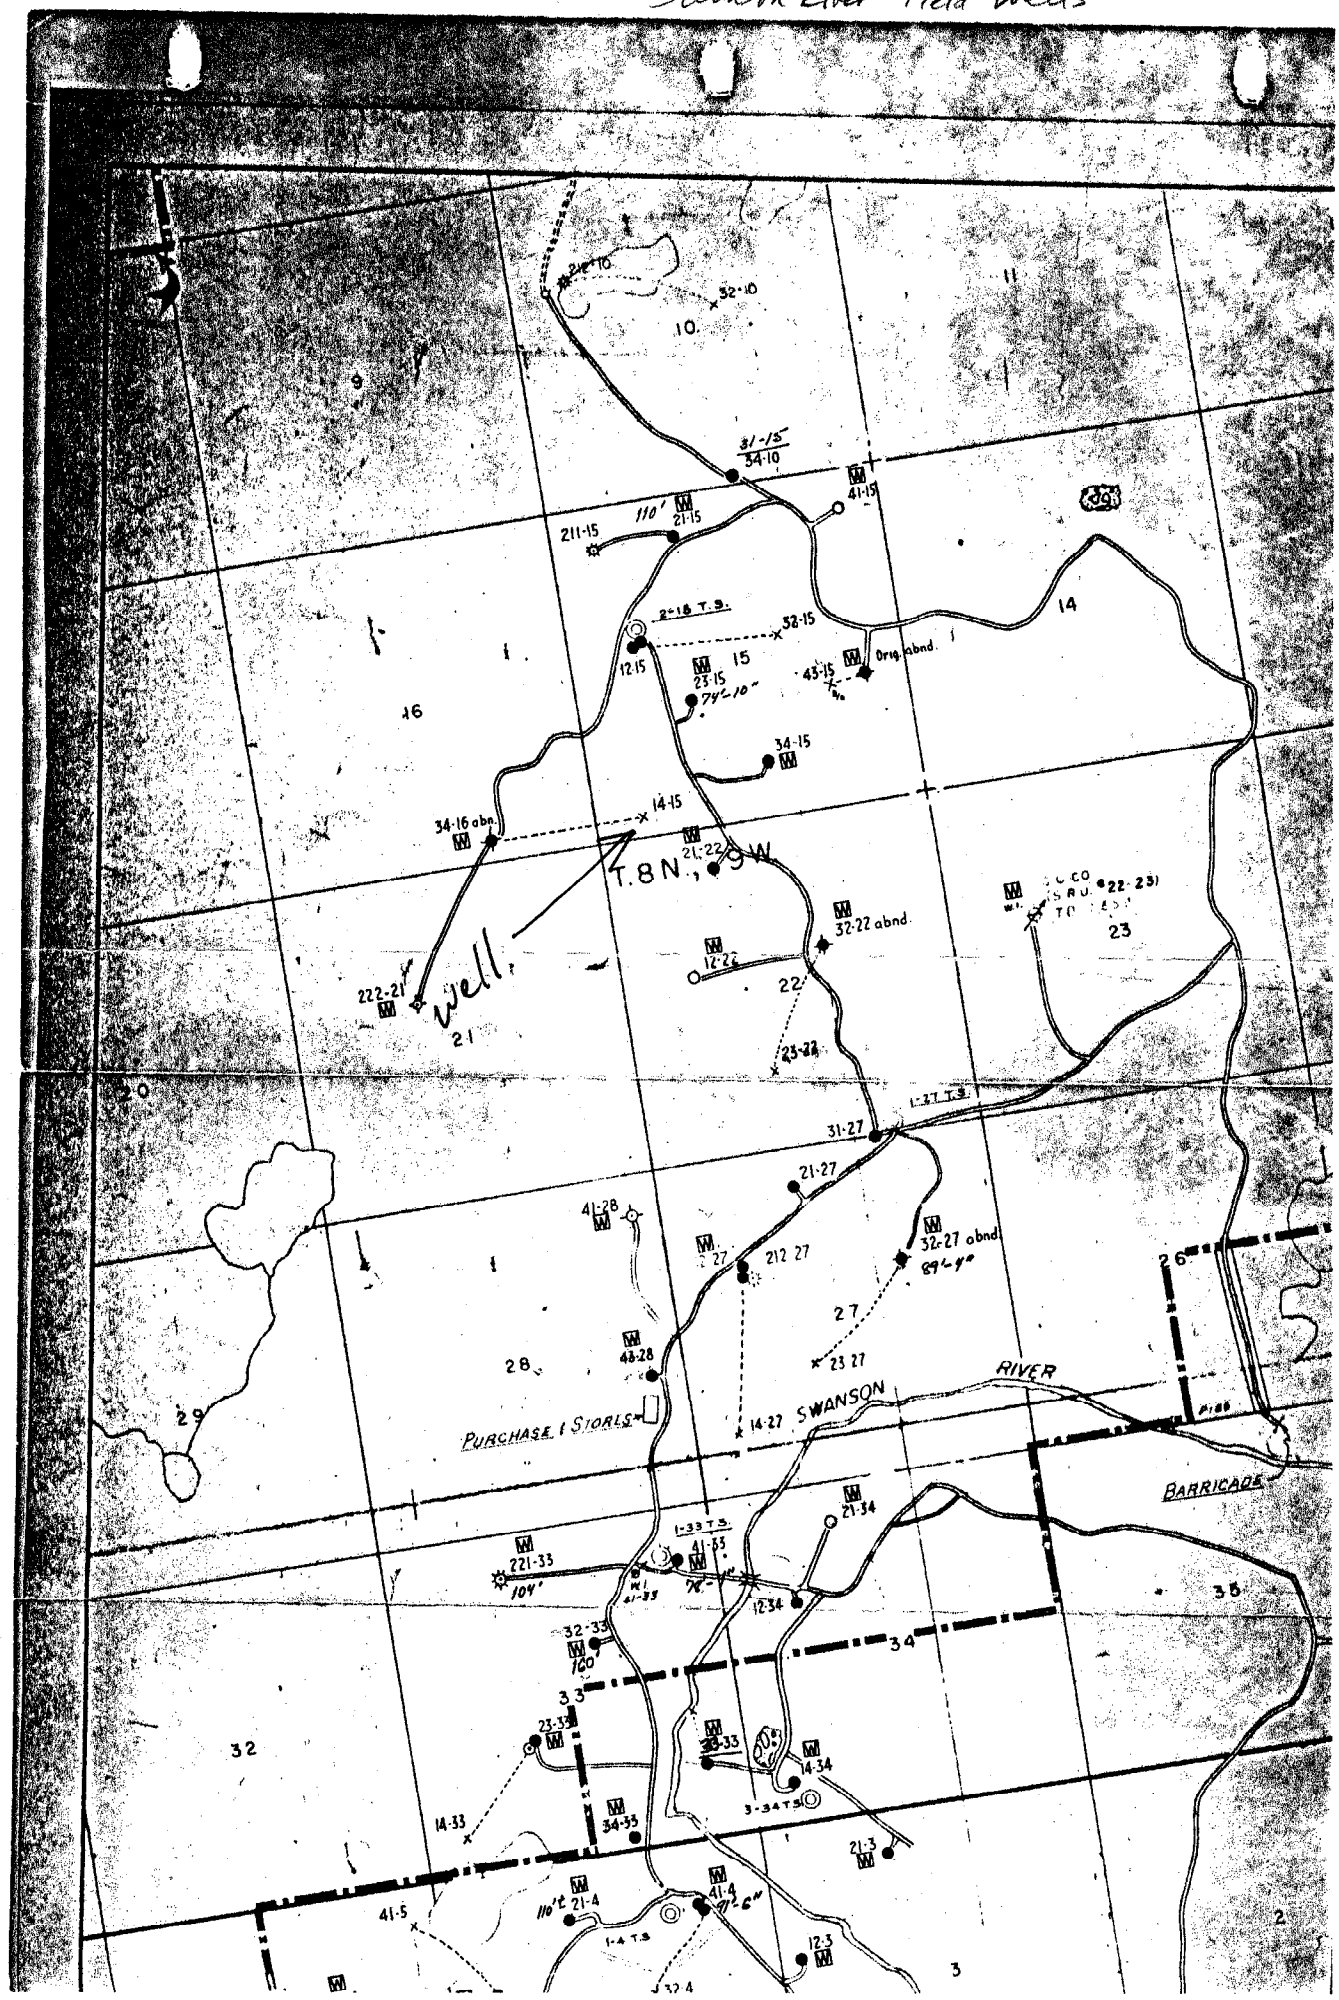

SB 8-9-15 CC
